Clarification Log

Project Number: P21050

Project Title: Island Park

Date	Question	Response
06/21/2013	**Attention: The day of the Mandatory Pre-bid meeting as shown in the Register Guard of Thursday June 26, 2013 is in error. The correct day of the meeting is Wednesday June 26, 2013.**	
06/28/13	Does the City want the contractor to connect the existing catch basins that are shown on the plans to the new stormwater system.	Yes. The contractor shall provide a connection between the two existing catch basins and the new stormwater system. Catch basin #1 (CB 1) can be connected to either the existing 36" concrete pipe, the new 36" concrete pipe or manhole #1 (MH - 1). Catch Basin #2 (CB 2) can be connected to the existing 36" concrete pipe, the new 18" PVC pipe, or MH-1. A diagram of a possible connection scenario is shown on the drawing following this page. The new connecting pipe shall be a minimum of 8" PVC.

P21050 ISLAND PARK

PROJECT DESCRIPTION

This project will consist of installing three manholes in the Water Street right of way, one of which is a a water quality MH. The work will include removing pipe, installing pipe, replacing a portion of curb and gutter, removing (2) driveway aprons and constructing (2) driveway aprons, removing guardrail, installing new guardrail, removing existing A.C. pavement as shown and paving A.C. as shown.

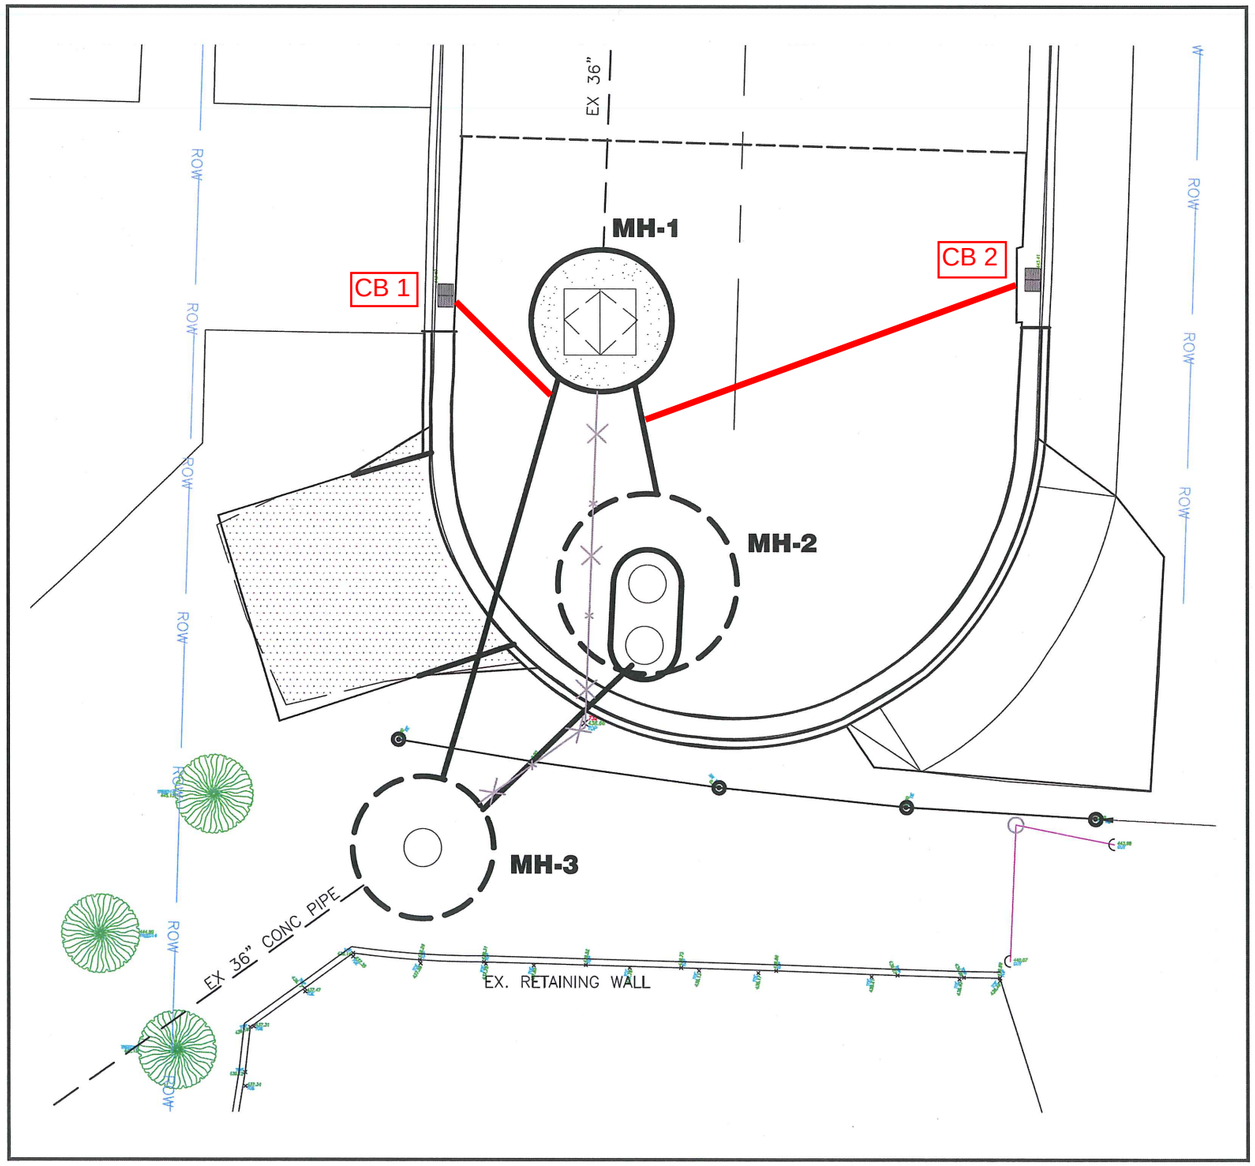

VICINITY MAP

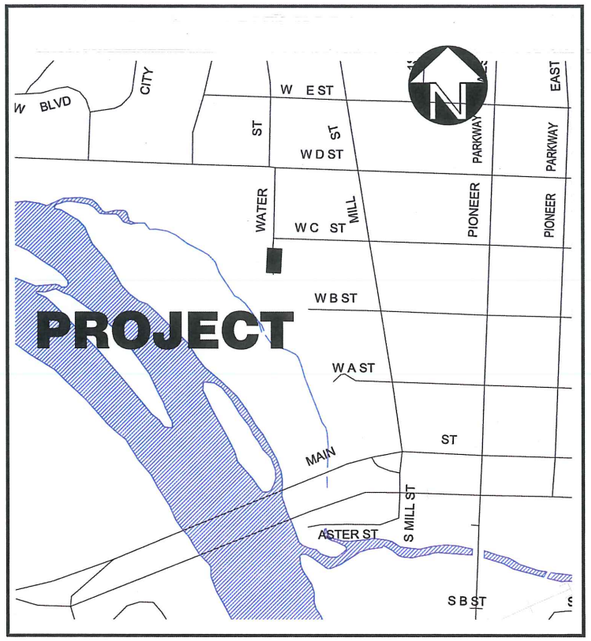

SHEET INDEX

TITLE SHEET	pg. 1
GENERAL NOTES	pg. 2
PLAN CONSTRUCTION	pg. 3
PAVING PLAN	pg. 4
DIAGRAM OVERVIEW	pg. 5
MH-1 INTERIOR WALLS	pg. 6
MH-1 SECTIONS	pg. 7
MH-3 SECTIONS	pg. 8
MH-2 RISER	pg. 9
EROSION CONTROL NOTES	pg. E1
EROSION CONTROL	pg. E2

No.	Revision/Issue	Date

NOTE:

UTILITY LOCATIONS ARE APPROXIMATE
DO NOT
SCALE OR LOCATE UTILITY LINES OR MAINS FROM THESE DRAWINGS
CALL FOR UTILITY LOCATES
811 or (1-800-332-2344)

THE CONTRACTOR SHALL BE RESPONSIBLE FOR DETERMINING UTILITY LOCATIONS PRIOR TO BEGINNING OF CONSTRUCTION.
THESE PLANS MAY NOT SHOW ALL UTILITIES OR THE CORRECT LOCATIONS.

P21050 ISLAND PARK

City of Springfield
PUBLIC WORKS / ENGINEERING
225 FIFTH STREET, SPRINGFIELD, OR 97477
PHONE (541) 726-3753 FAX (541) 736-1021
INTERNET www.ci.springfield.or.us

REGISTERED PROFESSIONAL ENGINEER
54699PE
Jeffrey Alan Paschall
OREGON
JULY 15, 2003
JEFFREY ALAN PASCHALL

EXPIRATION DATE: 12/31/2014

Scale

SHEET
1
